

RECEIVED
OCT 03 2013



486 E Street, Coos Bay, Oregon 97420
phone 541/266-8601 fax 541/266-8681

**Change Order No. 2
to the Contract for the Construction of
City of Newport – Roadway Improvement Project
SE Ash Street**

Item 2A– Contractor was given direction to raise and/ or adjust curb grade line from ~station 5+50 to station 7+00 to better match rim elevation of found manhole and entrance to local PUD facility.

Work was completed July 31, 2013 – Total cost as associated to adjust grades:

Add: \$5,233.82
Deduct: N/A

Item 2B – Contractor was given direction to adjust the existing sanitary sewer and extend the existing storm drain line from residence to existing storm drain manhole located at ~station 5+35.

Work was complete August 12, 2013 – Total cost as associated to extend existing storm line:

Add: \$3,970.16
Deduct: N/A

Item 2C – Pot hole and expose existing 60inch sanitary sewer manhole, remove flat top and top 2 foot section of manhole replace with new 1 foot manhole section reset flat top. Remove 42 inch sanitary sewer cone section and replace with 42 inch flat top lid, re-grade as required for curb and gutter.

Work was completed August 19, 2013 – Total cost as associated to remove and replace manhole sections:

Add: \$2,831.76
Deduct: N/A

Item 2D – Contractor was directed to extend found 8 inch storm drain line northerly to new area drain No2. Contractor installed and placed ~189 lineal feet of new 8 inch PVC storm drain line.

Total cost as associated to extend the existing 8” storm drain line, @\$65/ lf:

Add: \$12,285.00
Deduct: N/A


Item 2E – Omit/ delete the 60 lineal feet of 12 inch PVC 3034 Storm Drain pipe as shown on the Bid Form and replace with new 8 inch PVC 3034 Storm Drain pipe as stated above.

Total cost as associated with omitting the 12 inch storm drain pipe:

Add: N/A
Deduct: \$4,800.00

CHANGE TO THE CONTRACT AMOUNT:

ADD: \$24,320.70

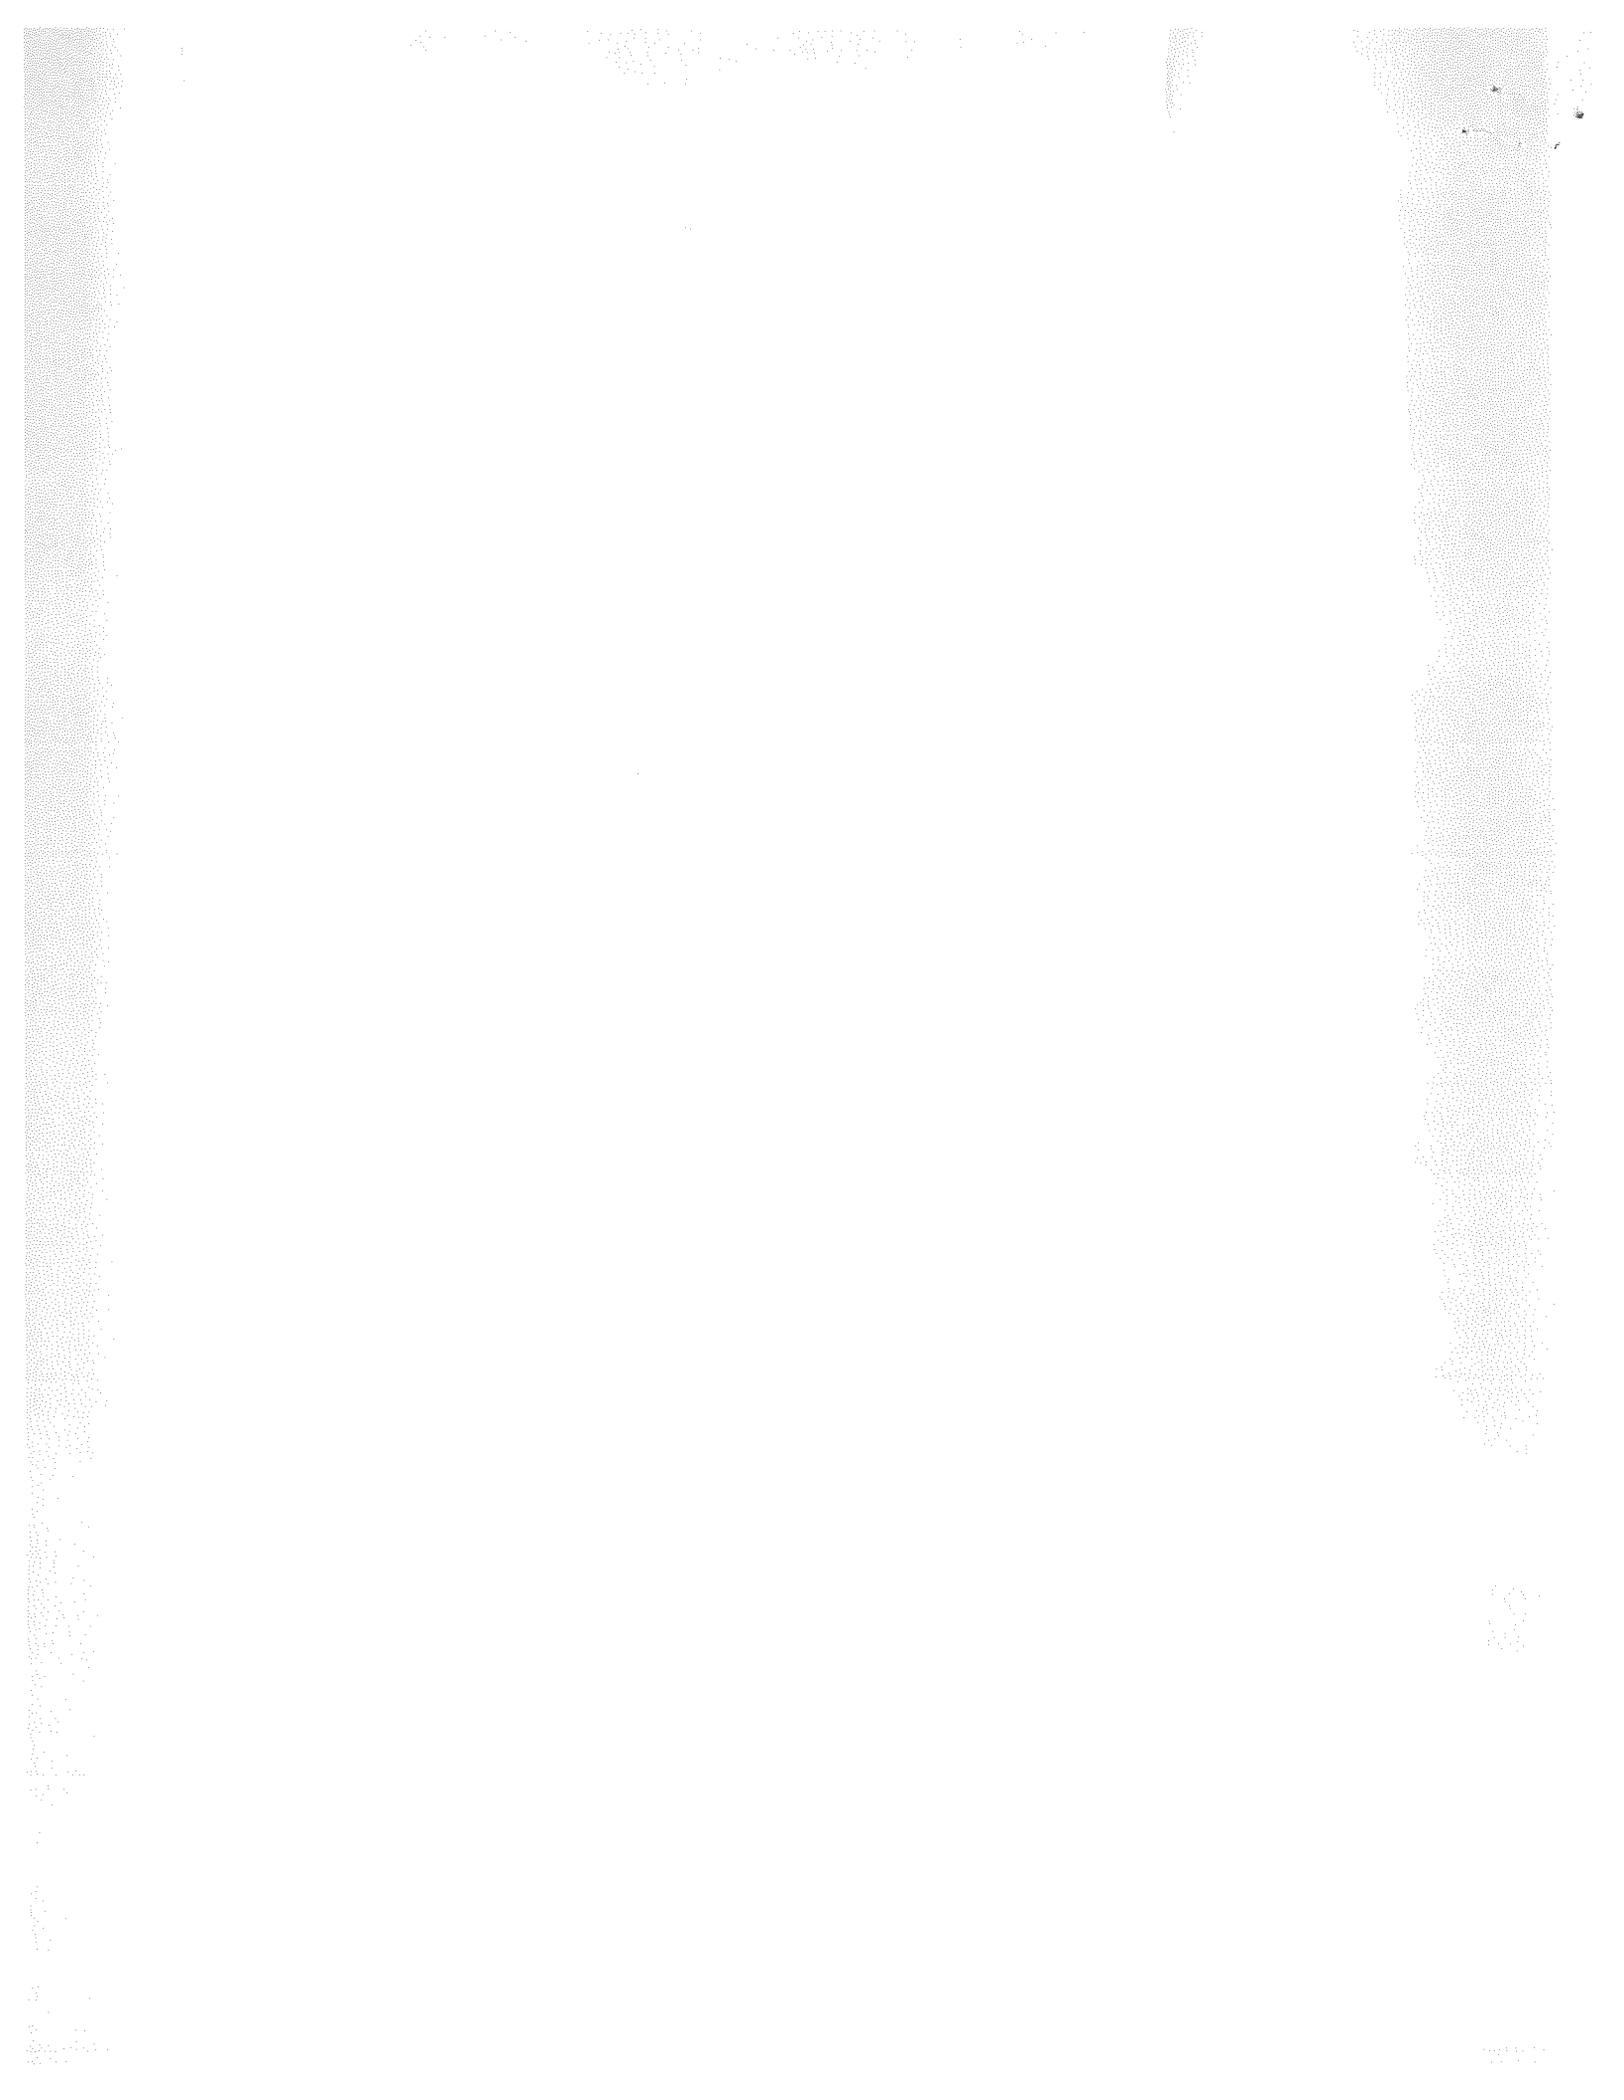

CHANGE TO THE CONTRACT AMOUNT:	DEDUCT:	\$4,800.00
TOTAL CHANGE TO THE CONTRACT AMOUNT:	ADD:	\$19,520.74
CHANGE TO THE CONTRACT TIME:	ADD:	0 Days

CHANGE IN CONTRACT PRICE:	CHANGE IN CONTRACT TIMES:
Original Contract Price:	Original Contract Times: <input type="checkbox"/> Working days <input checked="" type="checkbox"/> Calendar days
<u>\$ 330,296.00</u>	Substantial completion (DAYS or date): <u>120 Days</u>
	Ready for final payment (DAYS or date): <u>180 Days</u>
[Increase] [Decrease] from previously approved Change Orders No. 1 to 2:	[Increase] [Decrease] from previously approved Change Orders No.(1) to No. (-):
<u>\$4,987.55</u>	Substantial completion (days): <u>No Change</u>
	Ready for final payment (days): <u>No Change</u>
Contract Price prior to this Change Order:	Contract Times prior to this Change Order:
<u>\$ 335,283.55</u>	Substantial completion (days or date): <u>No Change</u>
	Ready for final payment (days or date): <u>No Change</u>
[Increase] [Decrease] of this Change Order:	[Increase] [Decrease] of this Change Order:
<u>Add: \$19,520.74</u>	Substantial completion (Days or date): <u>No Change</u>
	Ready for final payment (Days or date): <u>No Change</u>
Contract Price incorporating this Change Order:	Contract Times with all approved Change Orders:
<u>\$ 354,804.29</u>	Substantial completion (days or date): <u>No Change</u>
	Ready for final payment (days or date): <u>No Change</u>

RECOMMENDED:	ACCEPTED:	ACCEPTED:
By: <u>Civil West Engineering Services</u>	By: <u>City of Newport</u>	By: <u>Clackamas Construction</u>
By: <u><i>Mark J. Hamilton</i></u> Engineer (Authorized Signature)	By: <u><i>Muriel Jones</i></u> Owner (Authorized Signature)	By: <u><i>Bobbie Mohler</i></u> Contractor (Authorized Signature)
Date: <u>Oct 8-13</u>	Date: <u>10/14/13</u>	Date: <u>10.1.13</u>

THE UNIVERSITY OF CHICAGO

PHILOSOPHY DEPARTMENT

PHILOSOPHY 101

LECTURE NOTES

BY [Name]

DATE [Date]

TOPIC [Topic]

SECTION [Section]

LECTURER [Lecturer]

LECTURE [Lecture]

DATE [Date]

TOPIC [Topic]

SECTION [Section]

LECTURER [Lecturer]

LECTURE [Lecture]

DATE [Date]

TOPIC [Topic]

SECTION [Section]

LECTURER [Lecturer]

LECTURE [Lecture]

DATE [Date]

TOPIC [Topic]
